

VISUALMEDIA, LTD. · 15 SEPTEMBER 2026

Pioneer Parking, Inc Projects

Corporate identity, the parking platform, and the website — where each one stands, what it costs, and the four decisions we need from you today.



TODAY

Three projects, one hour

01

Corporate identity

We built Pioneer a design standard so the products had something to follow. It is yours to adopt, or not.

02

The platform

Pioneer Passport is running. Today we agree the pilot scope, the timeline and the price.

03

The website

Built, and waiting on the identity. A separate, smaller piece of work.

Most of the hour belongs to the platform. It is the only item with a decision attached to a date.

01

SECTION ONE

Corporate identity

A standard we wrote on our own initiative, because the products needed one.

We built the standard the products needed

You cannot build four connected products without deciding what they look like. Rather than settle it screen by screen and reconcile the differences later, we wrote the standard first — **Pioneer Identity, Edition 1.1** — and built the platform against it.

THE WORK

Already done

Mark, colour, typography, iconography, contrast standards and digital tokens. In use in the running application today.

THE POSITION

Yours to adopt

If Pioneer adopts it as the company identity, it becomes yours outright. If not, it remains our internal build standard at no cost to you.



THE OFFER

We can complete it


Logo files in every format, licensed type, stationery, signage, vehicle and garage applications, and a guidelines document. Quoted separately.

Colour, and the rule that governs it

Red is rare, which is why it is noticed. It appears in the mark and in display type at 24px and above — never as body text, never as a button.

						
Pioneer Red #FD2F38 Mark and display only	Pioneer Navy #0B2C5D Headings, sign panels	Signal Blue #0048A8 Screens. Anything actionable	Asphalt #1A1F33 Body text	Concrete #5A6478 Secondary text	Line #E2E4E8 Dividers and rules	Paper #F2F4F8 The ground

PROPORTION



Paper 58 · Navy 26 · Blue 8 · Red 6

Typography

DISPLAY

Overpass

Drawn from Highway Gothic — the lettering on American road signs. It belongs on a parking structure. Headings, wayfinding, buttons, labels.

CODES

PP-1248


Overpass Mono for decal numbers, ticket codes and times. Every digit the same width, so nothing shifts as a number changes.

INTERFACE

Source Sans 3

Everything a person reads rather than scans. Source Serif 4 handles correspondence. All four families are open-licensed — **no licence fees, ever, on any number of devices.**

The standard, applied in the product

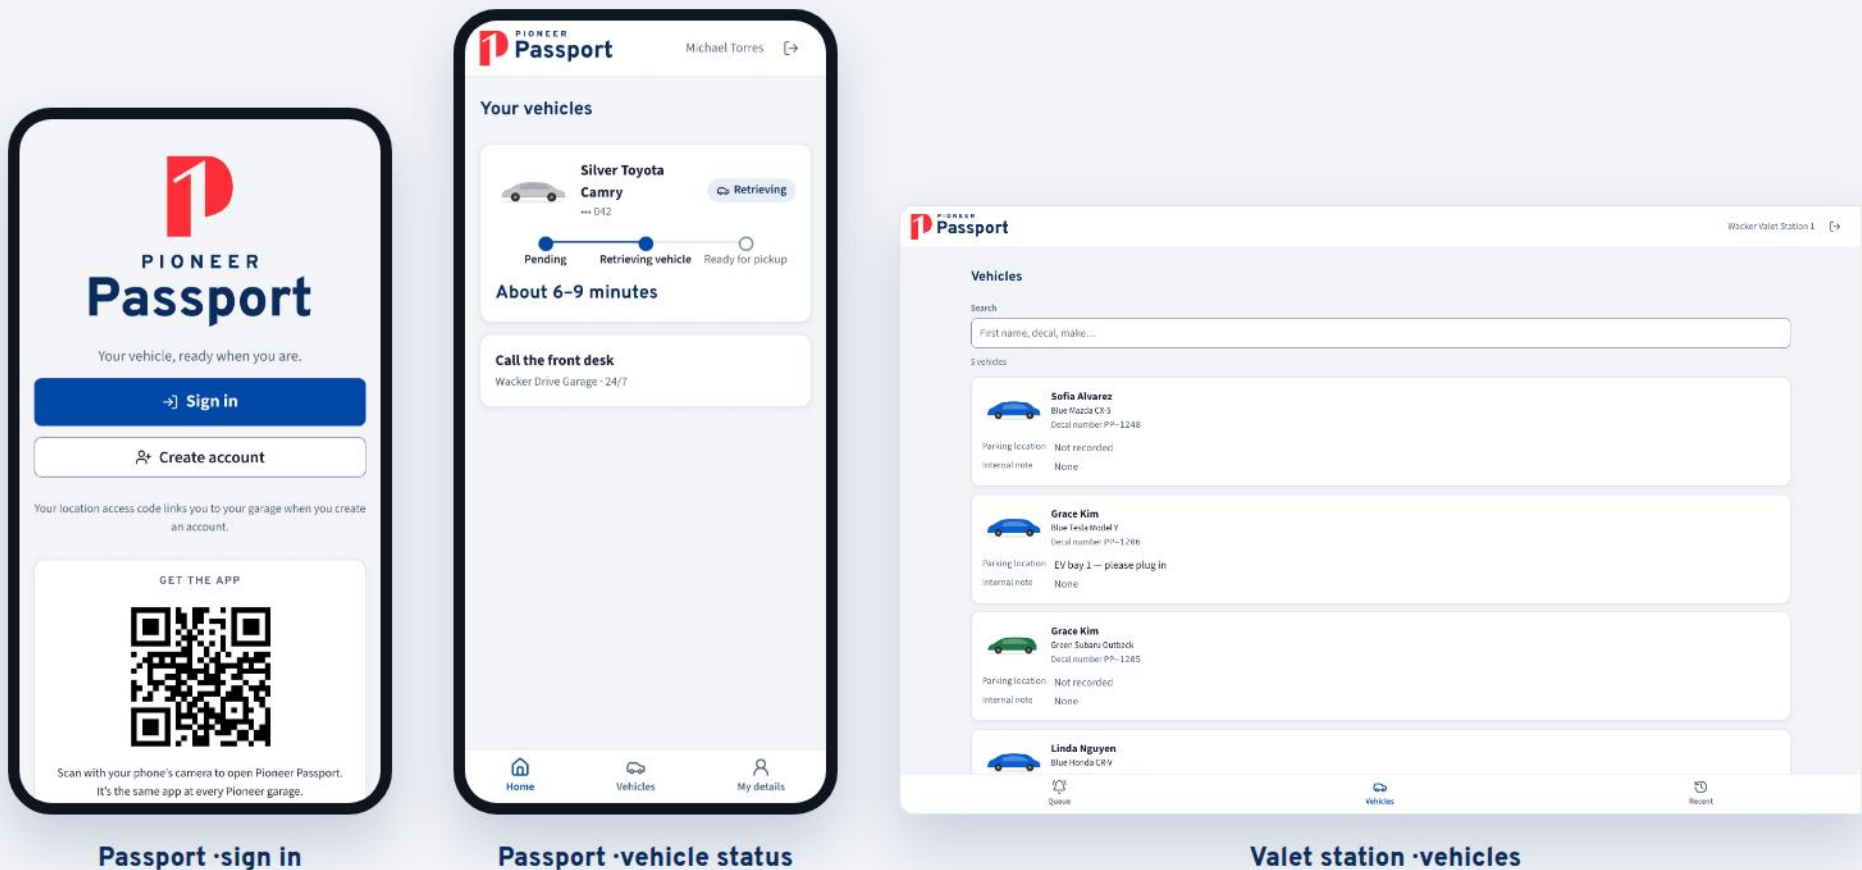

Every colour, every typeface and every contrast pair on these screens comes from the standard. It was applied as the product was built, rather than retrofitted afterwards.

02

SECTION TWO

The platform

Pioneer Passport. What is built, what the pilot covers, what it costs.

One system, four audiences

LIVE

Passport — residents

Request the car. Watch it come. Three states, one estimate, nothing else to learn.

LIVE

Valet station

The queue, the vehicles, the recent history. Names and decals — never a phone number.

PHASE 2

Manager console

Approvals, overrides, staff, reports. One place to run a garage.


PHASE 2

Custody record

Every action signed and time-stamped. The answer when a customer disputes a scratch.

The data model is multi-tenant from day one. That is deliberate: it is what would let Pioneer license this platform to other operators rather than only run it.

The retrieval loop, end to end

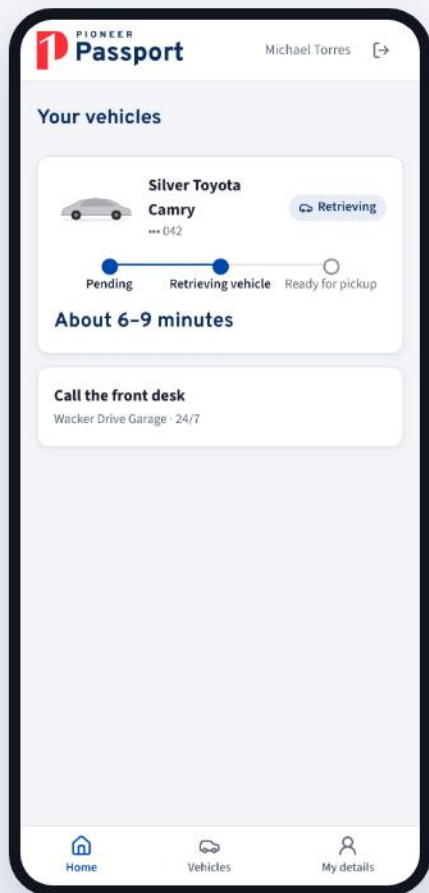

- ✓ A resident opens Passport and sees **their own vehicle**, by make, model and colour, with the decal masked.
- ✓ One tap requests it. The request lands on the valet station queue immediately.
- ✓ The stepper moves — **Pending** → **Retrieving vehicle** → **Ready for pickup** — with an honest estimate rather than a spinner.
- ✓ An attendant sees the name, the decal, the parking location and any internal note. **Never a phone number.**
- ✓ Every state change is written to an append-only log.

What the pilot is actually testing

Whether a resident trusts the estimate enough to stop calling the front desk. The screens already work; that behaviour is the question worth seven weeks.

What the pilot includes

RESIDENT

- ✓ Sign in, vehicles, request retrieval
- ✓ Live status with an honest estimate
- ✓ Push notification when the car is ready
- ✓ Native app, iOS and Android, internal distribution

ATTENDANT

- ✓ Queue, vehicles and recent history
- ✓ Accept · Ready · Complete · Revert
- ✓ The chime — repeats until accepted, cannot be disabled

PLATFORM

- ✓ Multi-tenant data model and location scoping
- ✓ Real-time updates, with an honest stale-state banner on reconnect
- ✓ Append-only activity log
- ✓ Manager status override, with an audit event

One garage, seeded by hand

One location, one valet station account, residents and vehicles entered by us. That is what keeps it to seven weeks — and it is the subject of the decision two slides from now.

What the pilot leaves out – on purpose

EXCLUDED	WHY	LANDS IN
Manager & admin consoles	One location, administered by hand	Phase 2
Approvals & manager-absence backup	Only needed once residents register themselves	Phase 2
Scheduled and future pickups	Immediate retrieval is the promise; scheduling is an enhancement	Phase 3
Notification preferences	Ready-only, on by default, is the pilot configuration	Phase 3
The other four locations	One garage is the test	Phase 4
Public app-store release	Internal distribution removes two review cycles from the critical path	Phase 5
Accessibility audit, pen test, privacy review	External and formal — premature before the loop is proven	Phase 5

Every excluded item is deferred, not cancelled. The exclusions are what buy you an answer in seven weeks instead of eighteen.

Seven weeks to an answer

Week 1

Foundations and sign-off

Environments, tenancy, identity tokens, the seeded garage. Self-registration decision closes here.

Weeks 2 - 3

The retrieval loop

Request, queue, state machine, the chime, the activity log. The core of the product.

Week 4

Real time and push

Live status, reconnection, stale-state banner, native push on both platforms.

Week 5

Hardening

Edge cases, offline behaviour, the valet 7:1 contrast standard, device testing.

Week 6

Garage rehearsal

On-site with real attendants and real vehicles. The week that finds what a desk cannot.

Week 7

Pilot live

Residents onboarded, monitoring in place, daily readout to Pioneer.

Start within a week of sign-off and the pilot is running before the first week of November.

Should residents register themselves during the pilot?

A QR block already sits on the Passport sign-in screen. The question is not whether to build a QR code — it is whether the pilot carries **self-registration**: a location access code, an account the resident creates, and an approval step behind it.

OPTION A · BASE PILOT

\$26,000 – \$28,000

Seven weeks · residents seeded by us

Proves the retrieval loop. Seeding fifty residents in one garage takes an afternoon. Registration is not the thing anyone doubts.

OPTION B · WITH SELF-REGISTRATION

\$33,000 – \$35,000

Nine weeks · residents register themselves

Proves the loop **and** that residents can self-serve. If you intend to show the pilot to other operators, this is the difference between a product and a demo.

Our recommendation is Option A — unless the pilot has an audience beyond Pioneer. Either way, we need the answer before week one: approvals reach into the data model, and adding them later costs more than the difference.

From one garage to the whole operation

Weeks 1 - 7

Everything in the pilot

Carried forward, not rebuilt.

Weeks 8 - 11

Identity and approvals

Self-registration with per-location codes, the three approval kinds, manager-absence backup with an escalation SLA.

Weeks 12 - 14

Manager console

Overrides, staff, vehicles, the custody record, reports in your existing formats.

Weeks 15 - 16

All five locations

Location administration, cross-location reporting, staff moves.

Weeks 17 - 18

Release

Public app-store submission, accessibility audit, penetration test, privacy review.

Scheduled pickups

Future and recurring retrieval — the commuter case.

Verified Custody Record

Condition captured at check-in and hand-back. Signed, time-stamped, and the answer to a disputed scratch.

Reports in your formats

Not ours. We need your current report layouts to build against.

What this would have cost, and what it costs

CONVENTIONAL BUILD

\$150,000 – \$200,000

Eighteen months ago, with a conventional team

The same scope, estimated line by line, at ordinary agency day rates. We cite it because it is the figure Pioneer arrived at independently.

VISUALMEDIA · PILOT

\$26,000 – \$28,000

Seven weeks · \$33,000 – \$35,000 with self-registration

Two things close the gap: **you already own a specification**, which removes the most expensive phase of any build, and we work AI-augmented, which compresses the rest.

NOT INCLUDED

Hosting and maintenance

A monthly retainer, quoted separately once the pilot scope is fixed.

NOT INCLUDED

Identity completion

The full asset and guidelines package, if Pioneer adopts the standard.

NOT INCLUDED

The website

Separate and smaller. Section three.

What we need from you

01

Your existing report formats

We will build reporting to match what your managers already use. We need the current layouts to do that.

02

The corporate video at full resolution

We are working from a low-resolution copy.

03

Photography of staff and garages

For the website and the identity applications. Real people in real locations beats anything we could buy.

04

Trademark clearance on the product names

Crew, **Console** and **Record** are our proposals. They are not in the build and should not be used publicly until your counsel clears them. **Passport** is already in use.

None of these block the pilot starting. All four block something later, so the sooner the better.

03

SECTION THREE

The website

Built. Waiting on one decision, not on development.

Where it stands

STATUS

The build is done

Structure, content and pages are complete. This is not a project waiting to start.

BLOCKED ON

The identity decision

Applying a standard Pioneer has not adopted would be premature. Section one decides this.

NEXT

Branding applied

Once the identity is settled, applying it to the site is a short, contained piece of work. We will quote it against the agreed standard.

We are deliberately not putting a number on this today. The scope depends on which way the identity decision goes, and a number set before that would not hold.

Four decisions

DECISION 01

Self-registration in the pilot?

Option A at \$26–28K over seven weeks, or Option B at \$33–35K over nine. We recommend A.

DECISION 02

Adopt the identity standard?

Yes, no, or yes-with-changes. A no costs nothing; it stays our internal build standard.

DECISION 03

Which garage runs the pilot?

We need the location, the attendants and roughly fifty residents.

DECISION 04

Start date

Sign-off plus one week. Everything downstream moves with this.

VisualMedia, Ltd.

dima@vismed3d.com
